




# Capital Improvements & Projects 2019 to 2023

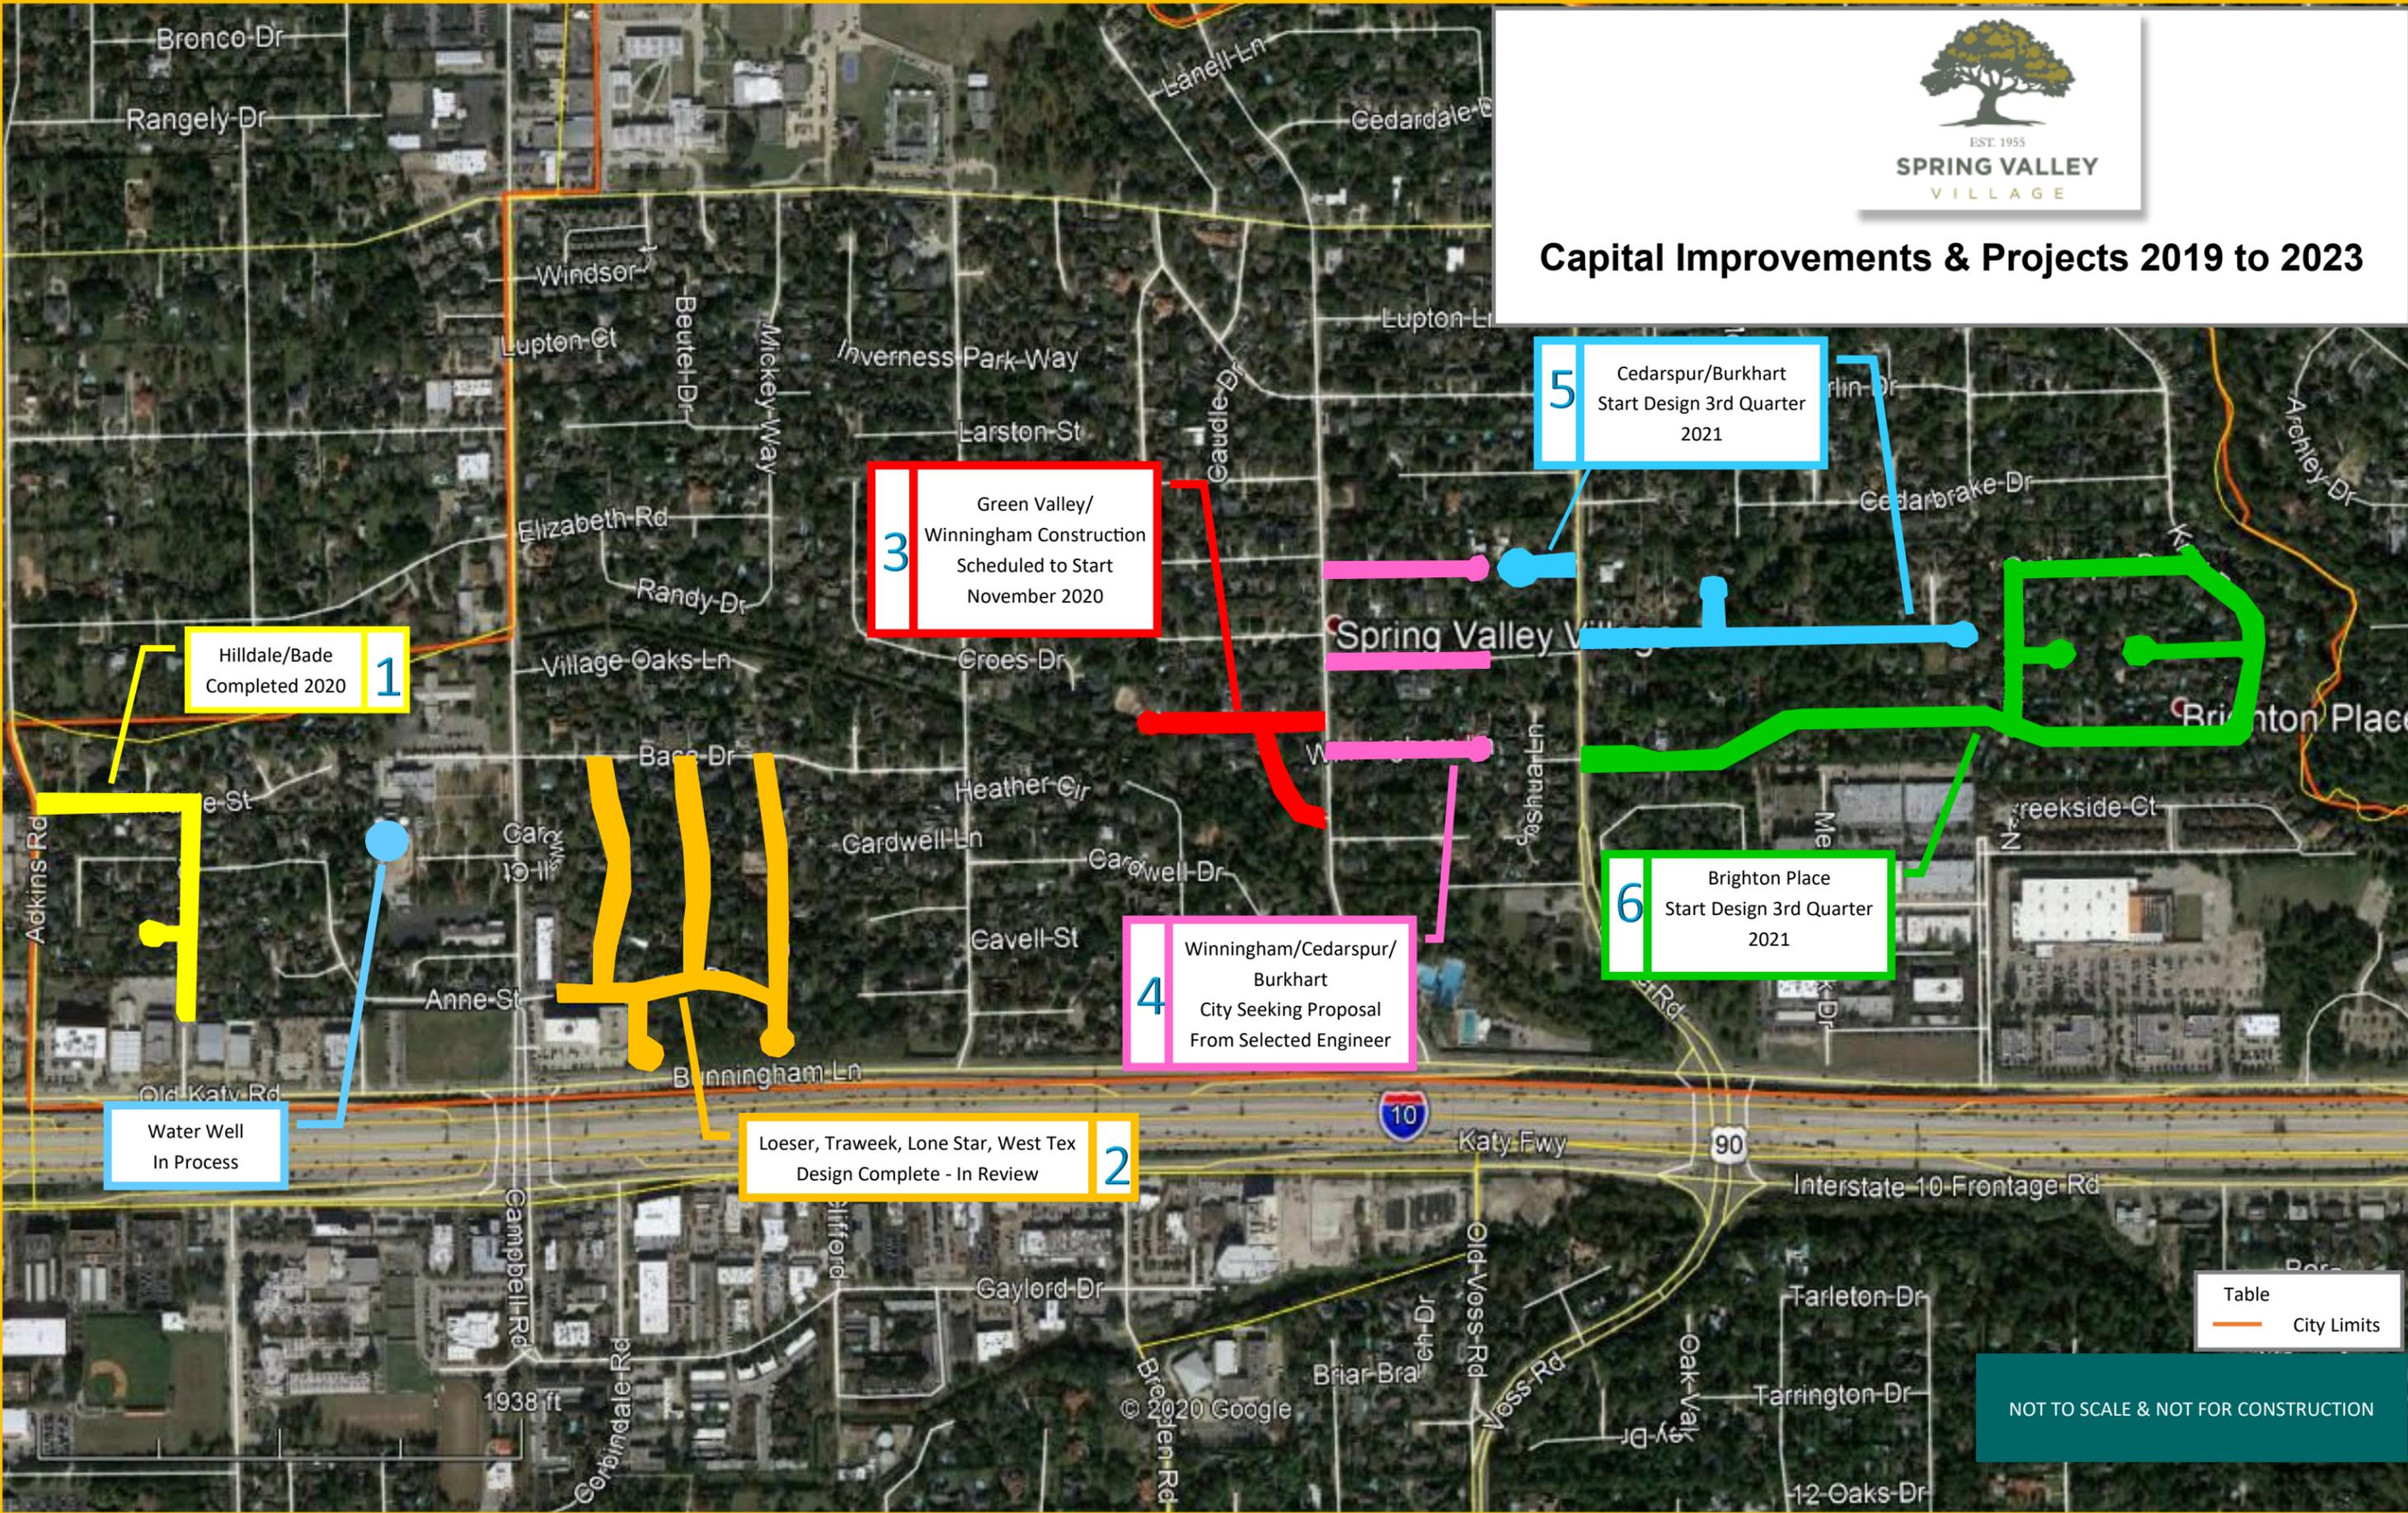

Hilldale/Bade  
Completed 2020 **1**

Water Well  
In Process

Loeser, Traweek, Lone Star, West Tex  
Design Complete - In Review **2**

Green Valley/  
Winningham Construction  
Scheduled to Start  
November 2020 **3**

Winningham/Cedarspur/  
Burkhart  
City Seeking Proposal  
From Selected Engineer **4**

Cedarspur/Burkhart  
Start Design 3rd Quarter  
2021 **5**

Brighton Place  
Start Design 3rd Quarter  
2021 **6**

Table  
City Limits

NOT TO SCALE & NOT FOR CONSTRUCTION

# New Production Water Well

Contract awarded to: W.W. Payton


Contract award date: March 26, 2019

Project Estimated Completion Date: March 2021

Due to a change in design for the electrical and chemical structure, the water well project estimated completion date has been extended to March 2021



NOT TO SCALE & NOT FOR CONSTRUCTION

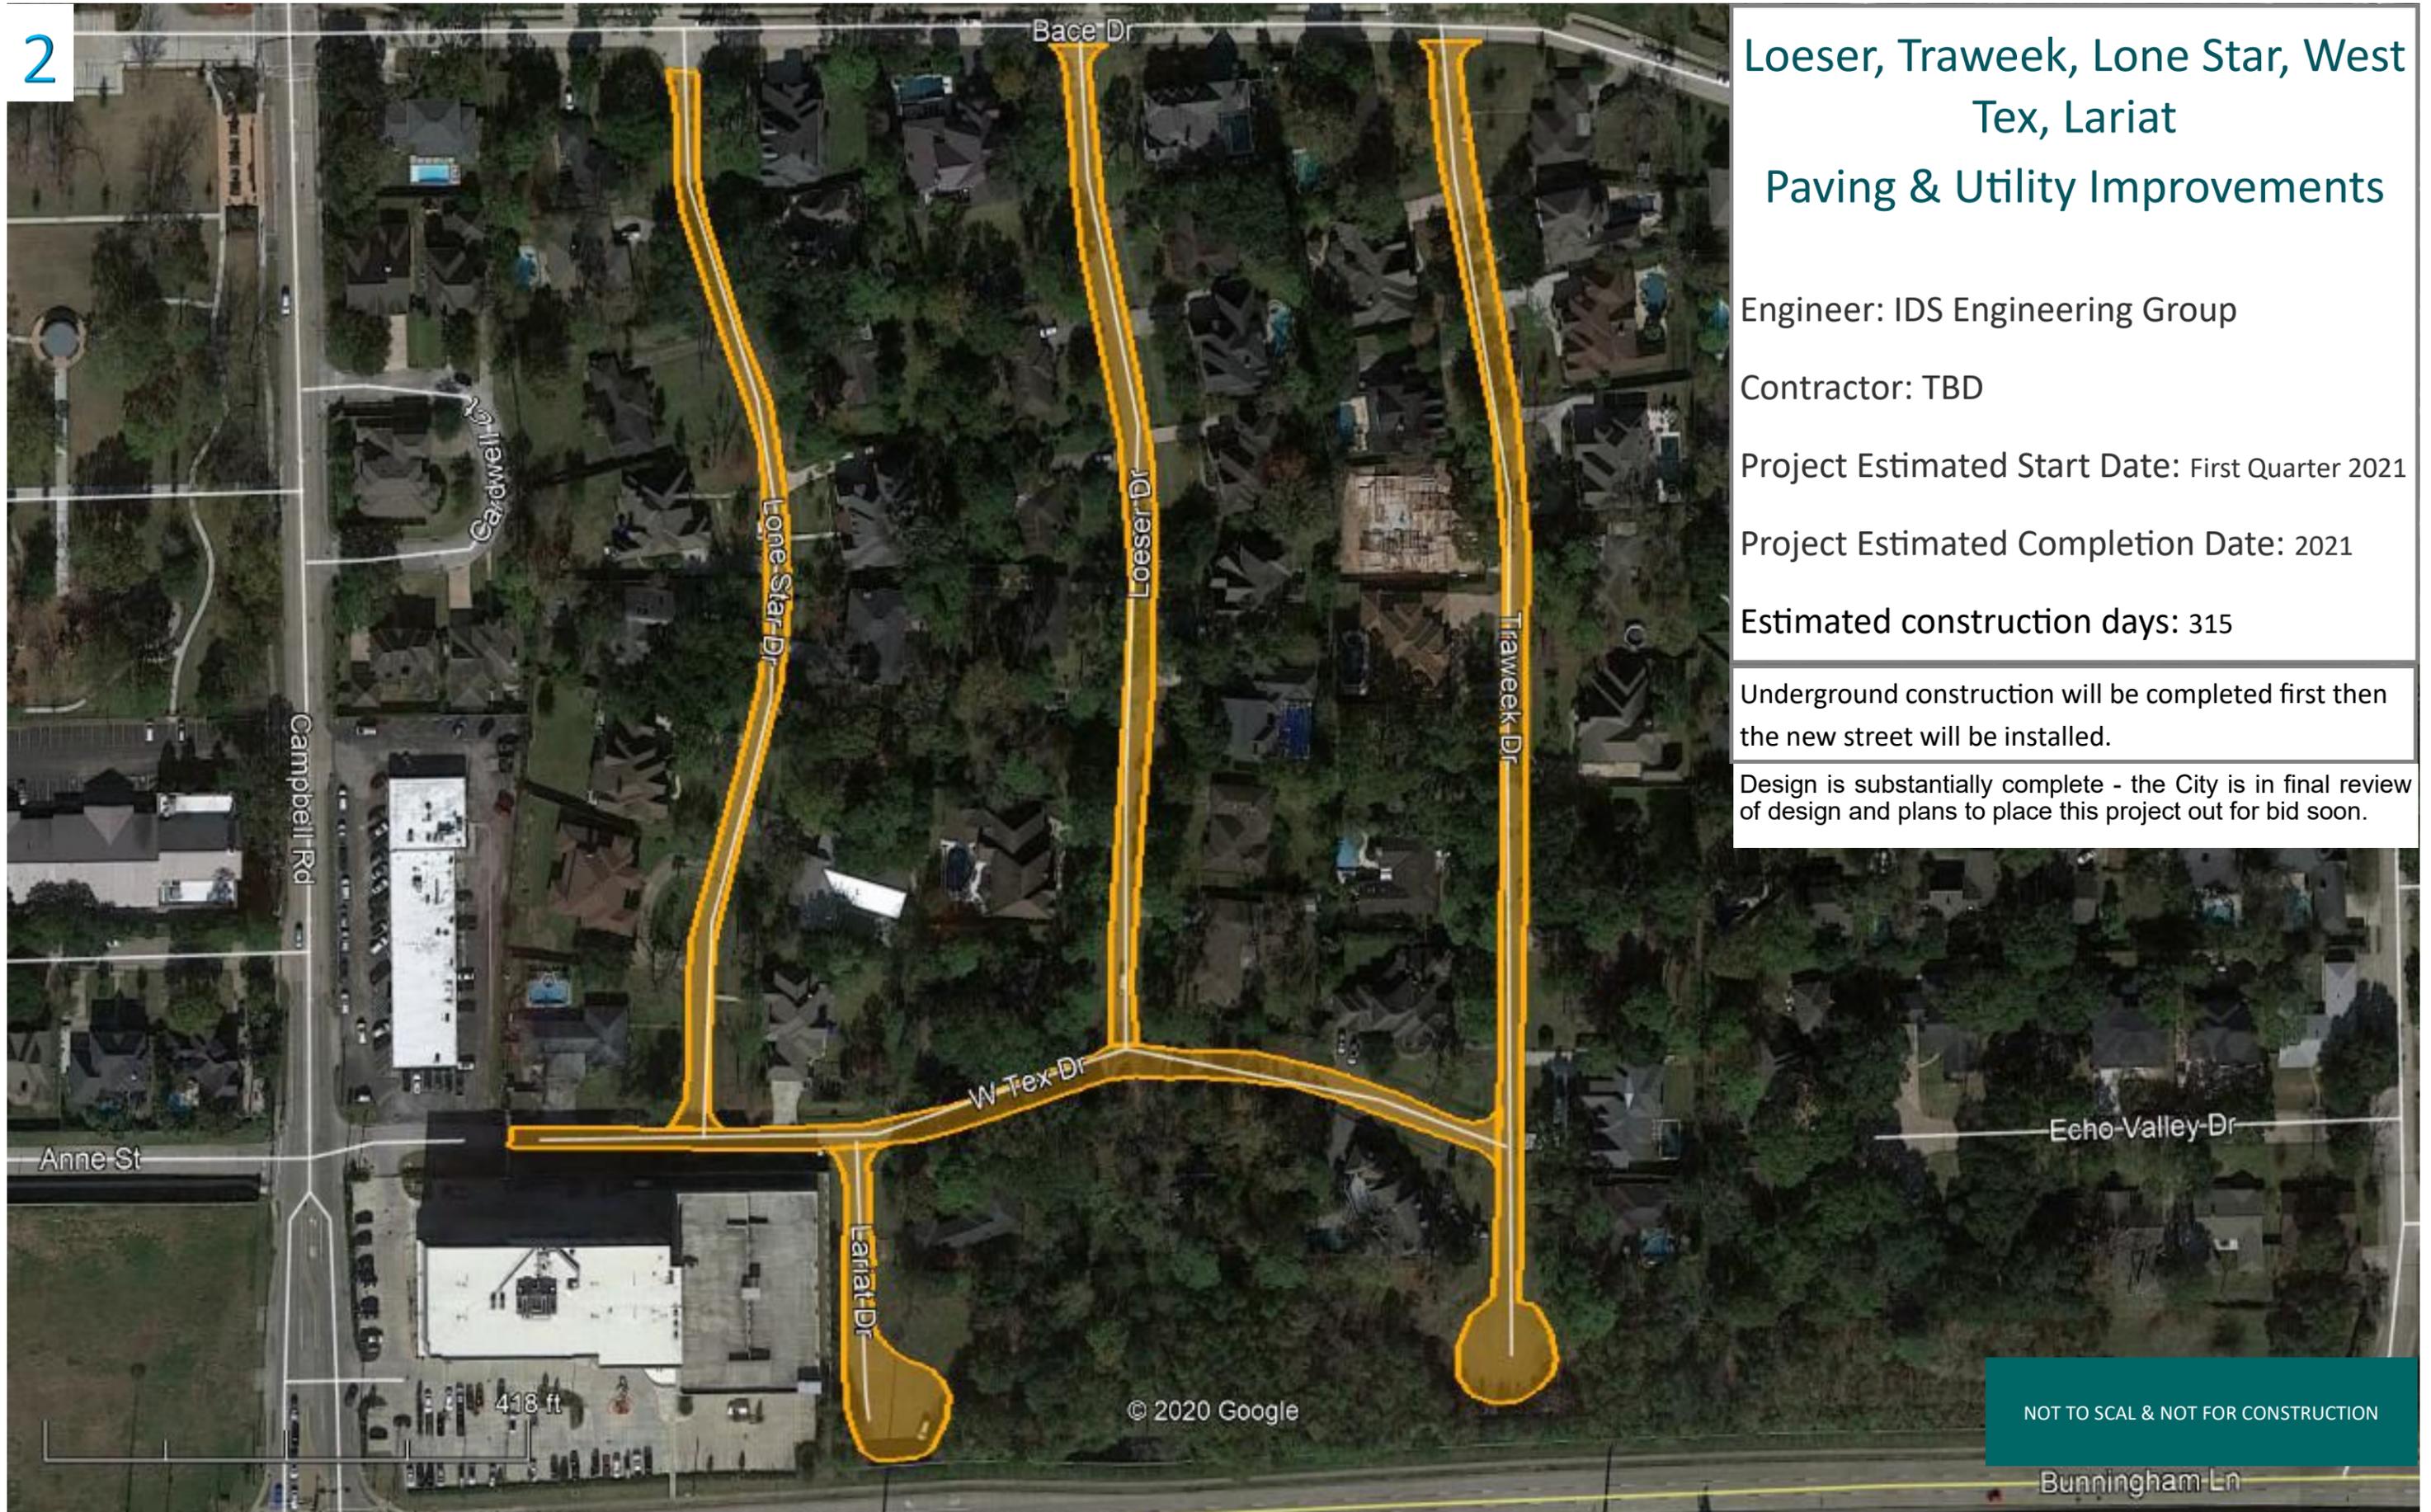

# Loeser, Traweek, Lone Star, West Tex, Lariat Paving & Utility Improvements

Engineer: IDS Engineering Group

Contractor: TBD

Project Estimated Start Date: First Quarter 2021

Project Estimated Completion Date: 2021


Estimated construction days: 315

Underground construction will be completed first then the new street will be installed.

Design is substantially complete - the City is in final review of design and plans to place this project out for bid soon.

NOT TO SCAL & NOT FOR CONSTRUCTION

Bunningham Ln

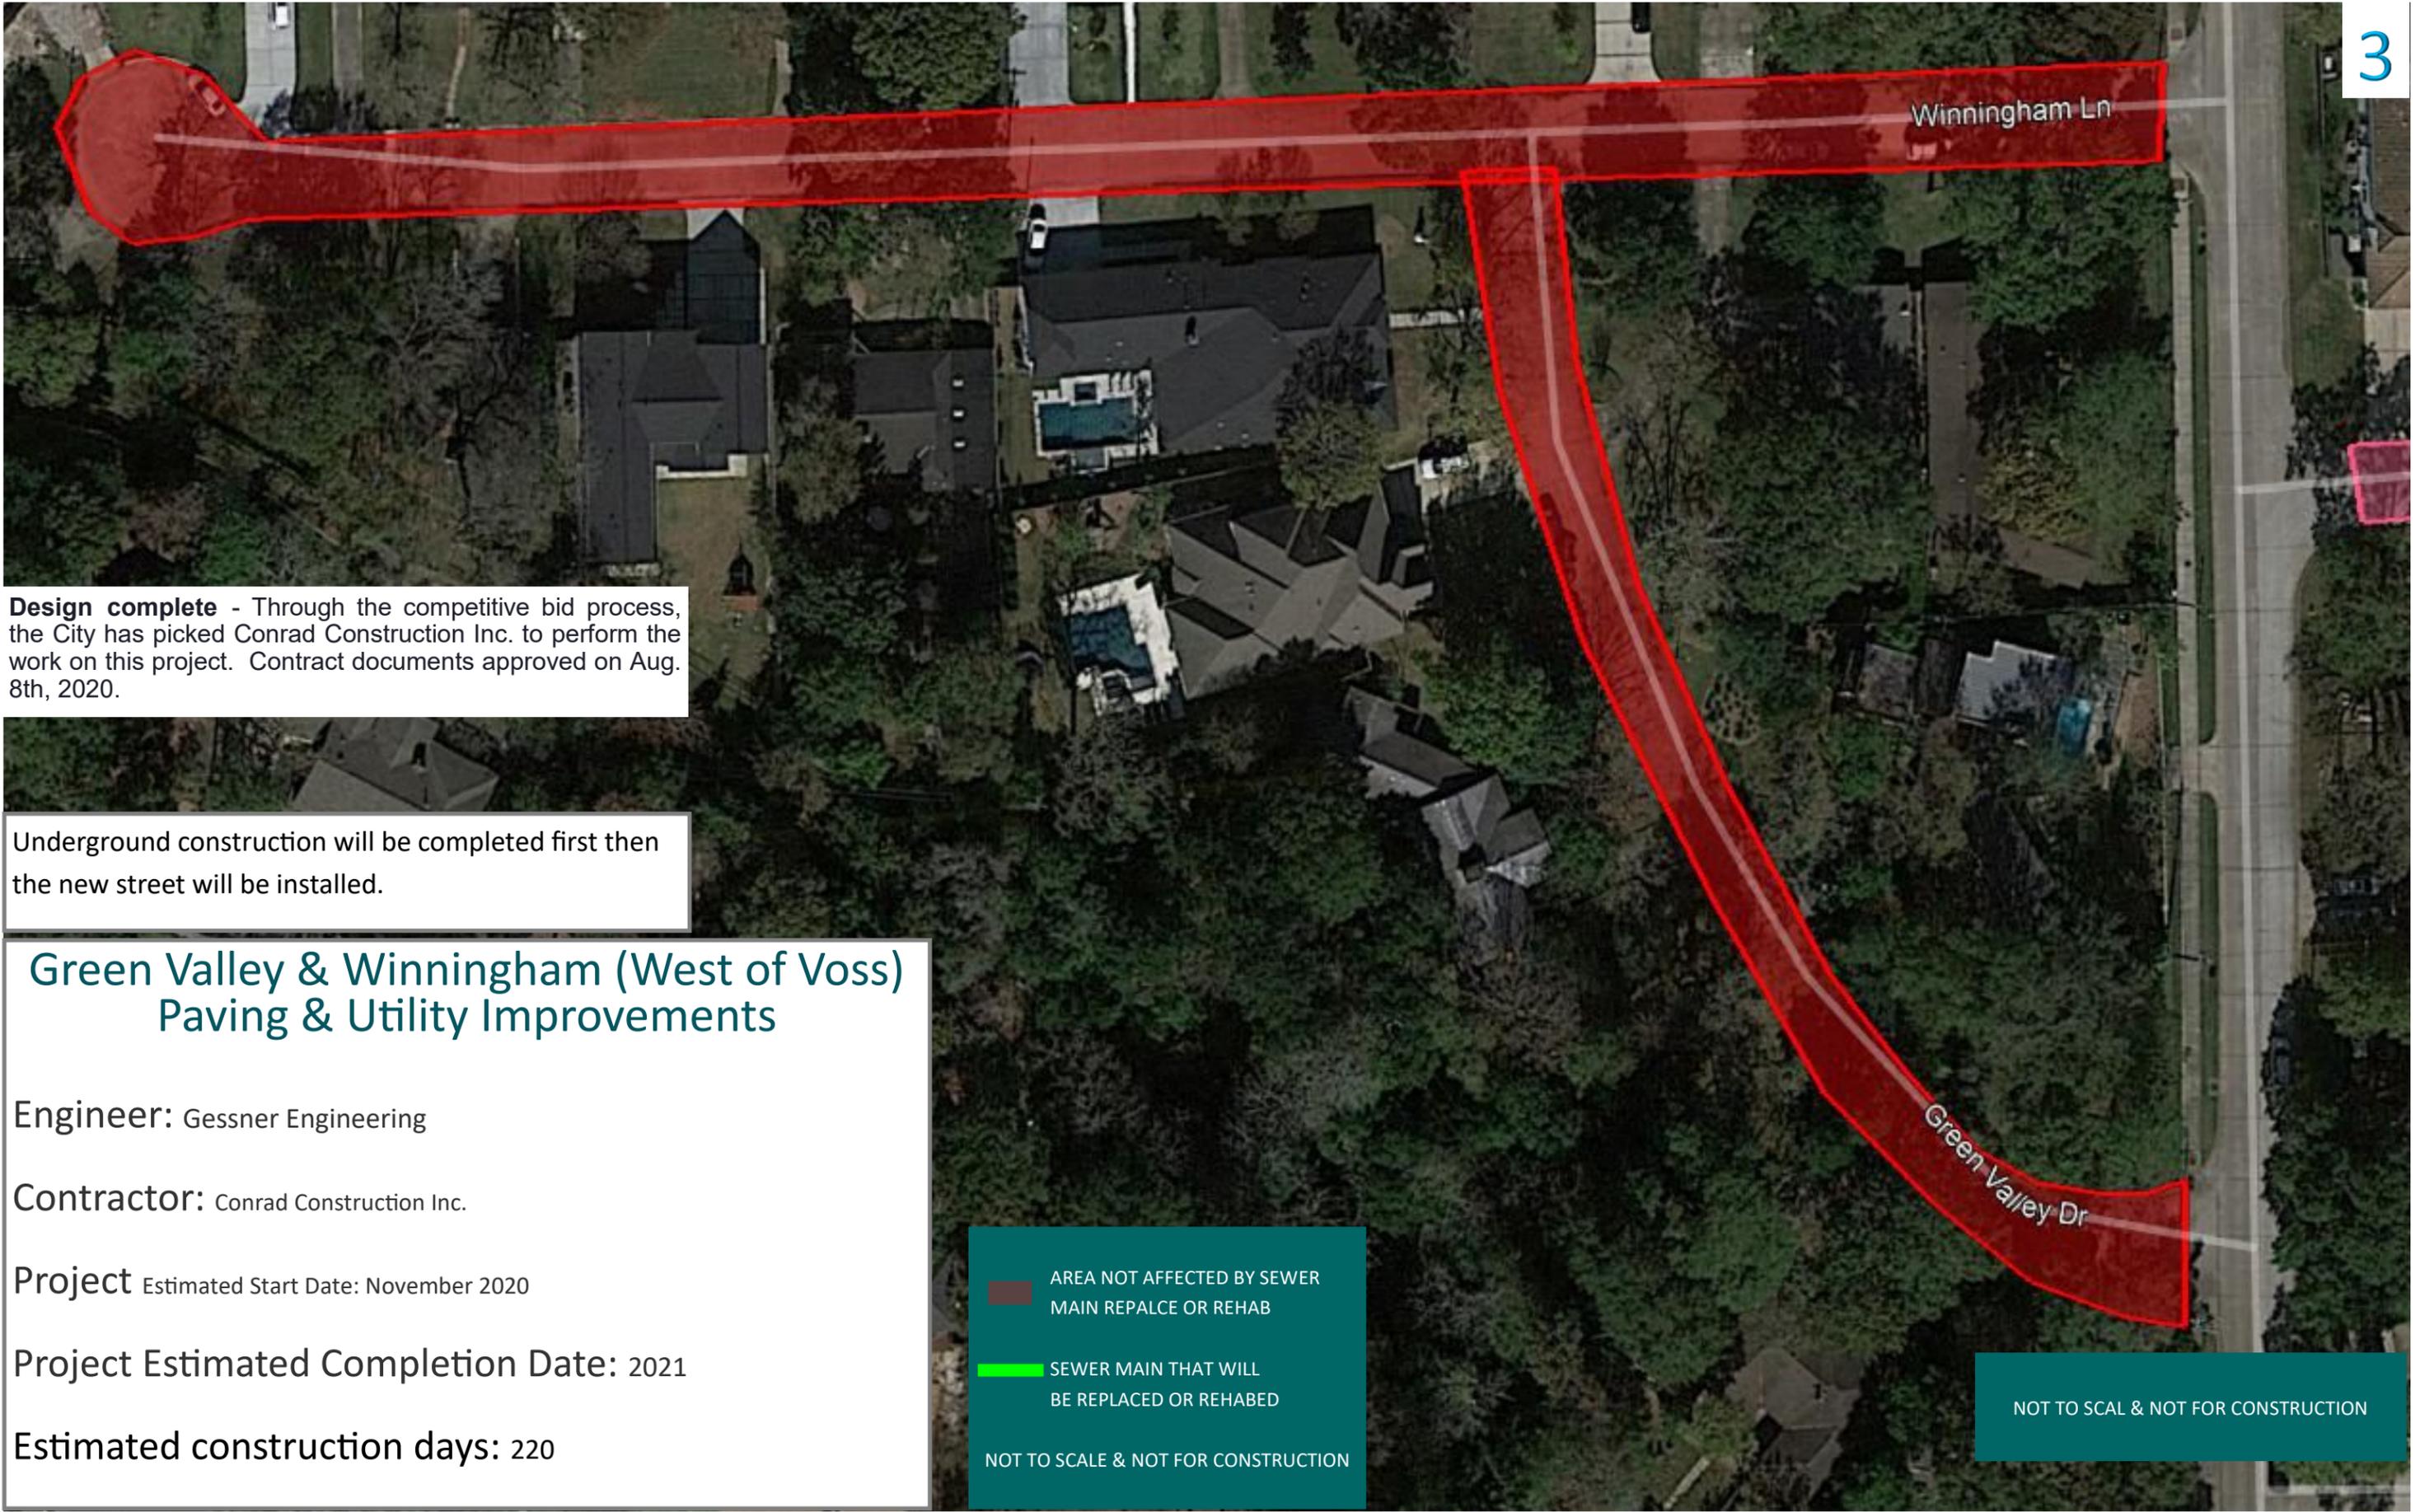

**Design complete** - Through the competitive bid process, the City has picked Conrad Construction Inc. to perform the work on this project. Contract documents approved on Aug. 8th, 2020.

Underground construction will be completed first then the new street will be installed.

### Green Valley & Winningham (West of Voss) Paving & Utility Improvements

Engineer: Gessner Engineering

Contractor: Conrad Construction Inc.

Project Estimated Start Date: November 2020

Project Estimated Completion Date: 2021

Estimated construction days: 220

 AREA NOT AFFECTED BY SEWER MAIN REPLACEMENT OR REHAB  
 SEWER MAIN THAT WILL BE REPLACED OR REHABED  
 NOT TO SCALE & NOT FOR CONSTRUCTION

NOT TO SCALE & NOT FOR CONSTRUCTION

# Winningham, Cedarspur & Burkhart (East of Voss) Paving & Utility Improvements


Engineer: Binkley & Barfield, Inc.

Contractor: TBD


Project Estimated Start Date: TBD

Project Estimated Completion Date: TBD

Underground construction will be completed first then the new street will be installed.

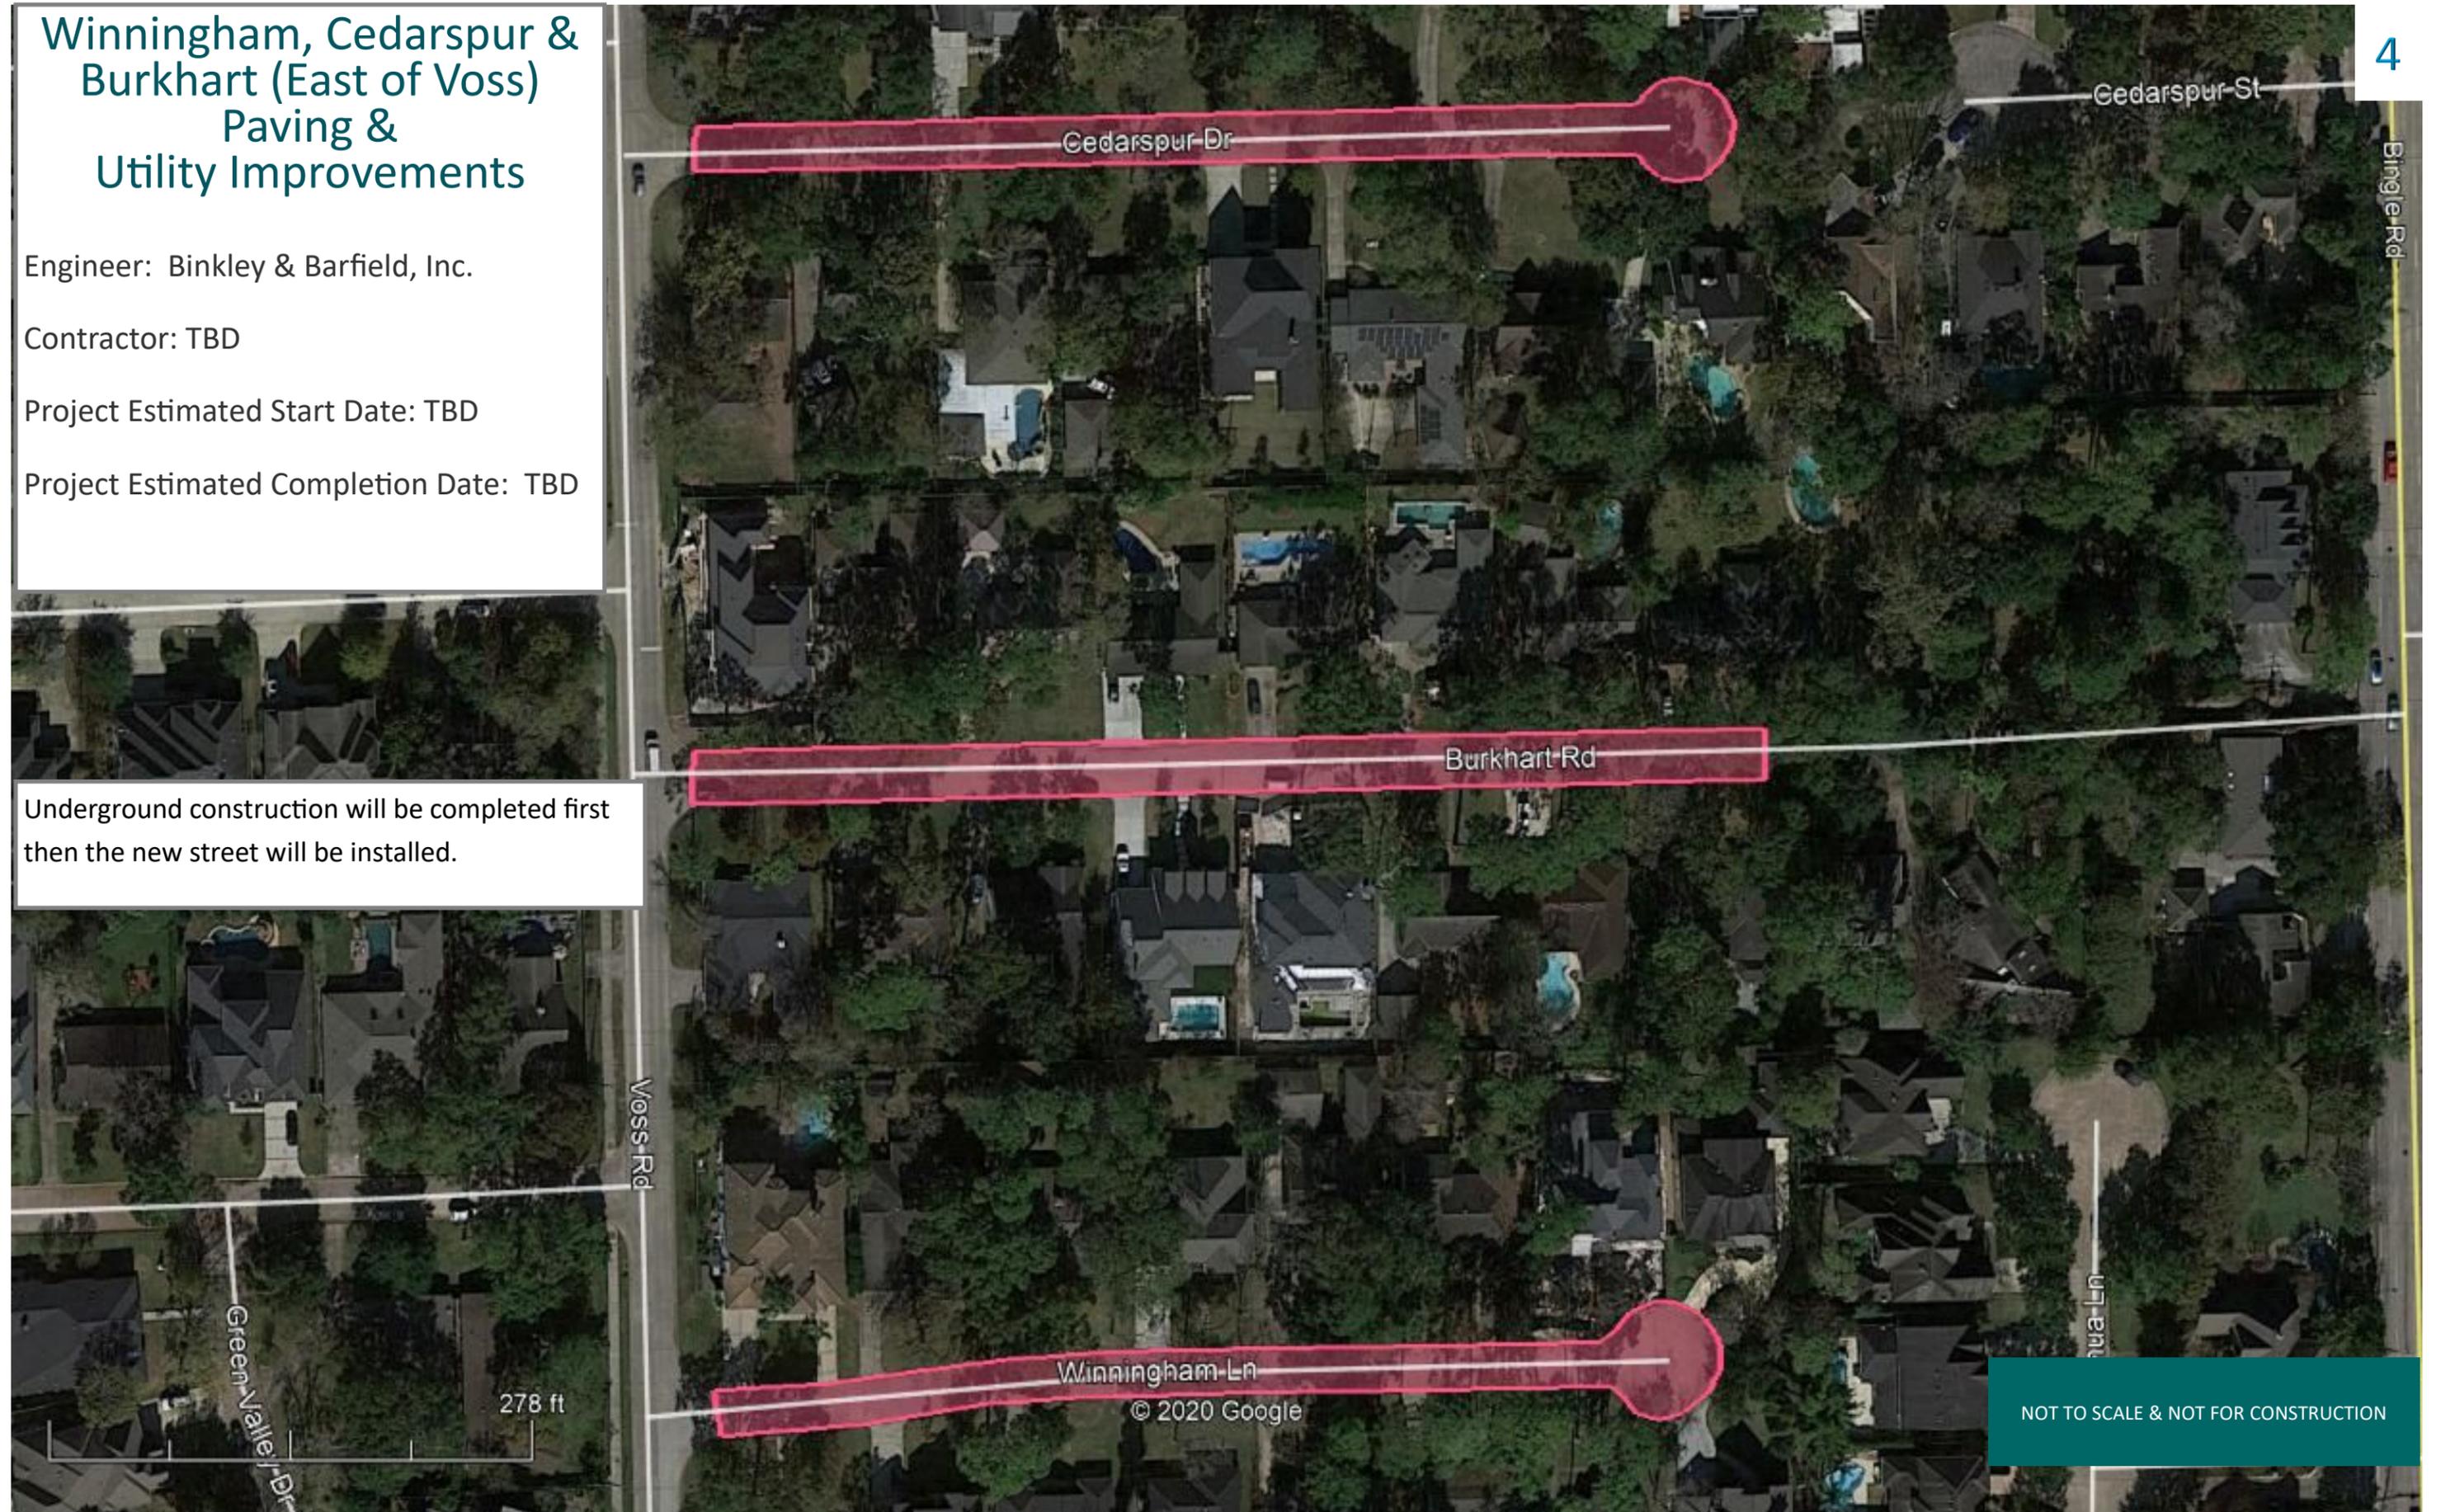

NOT TO SCALE & NOT FOR CONSTRUCTION

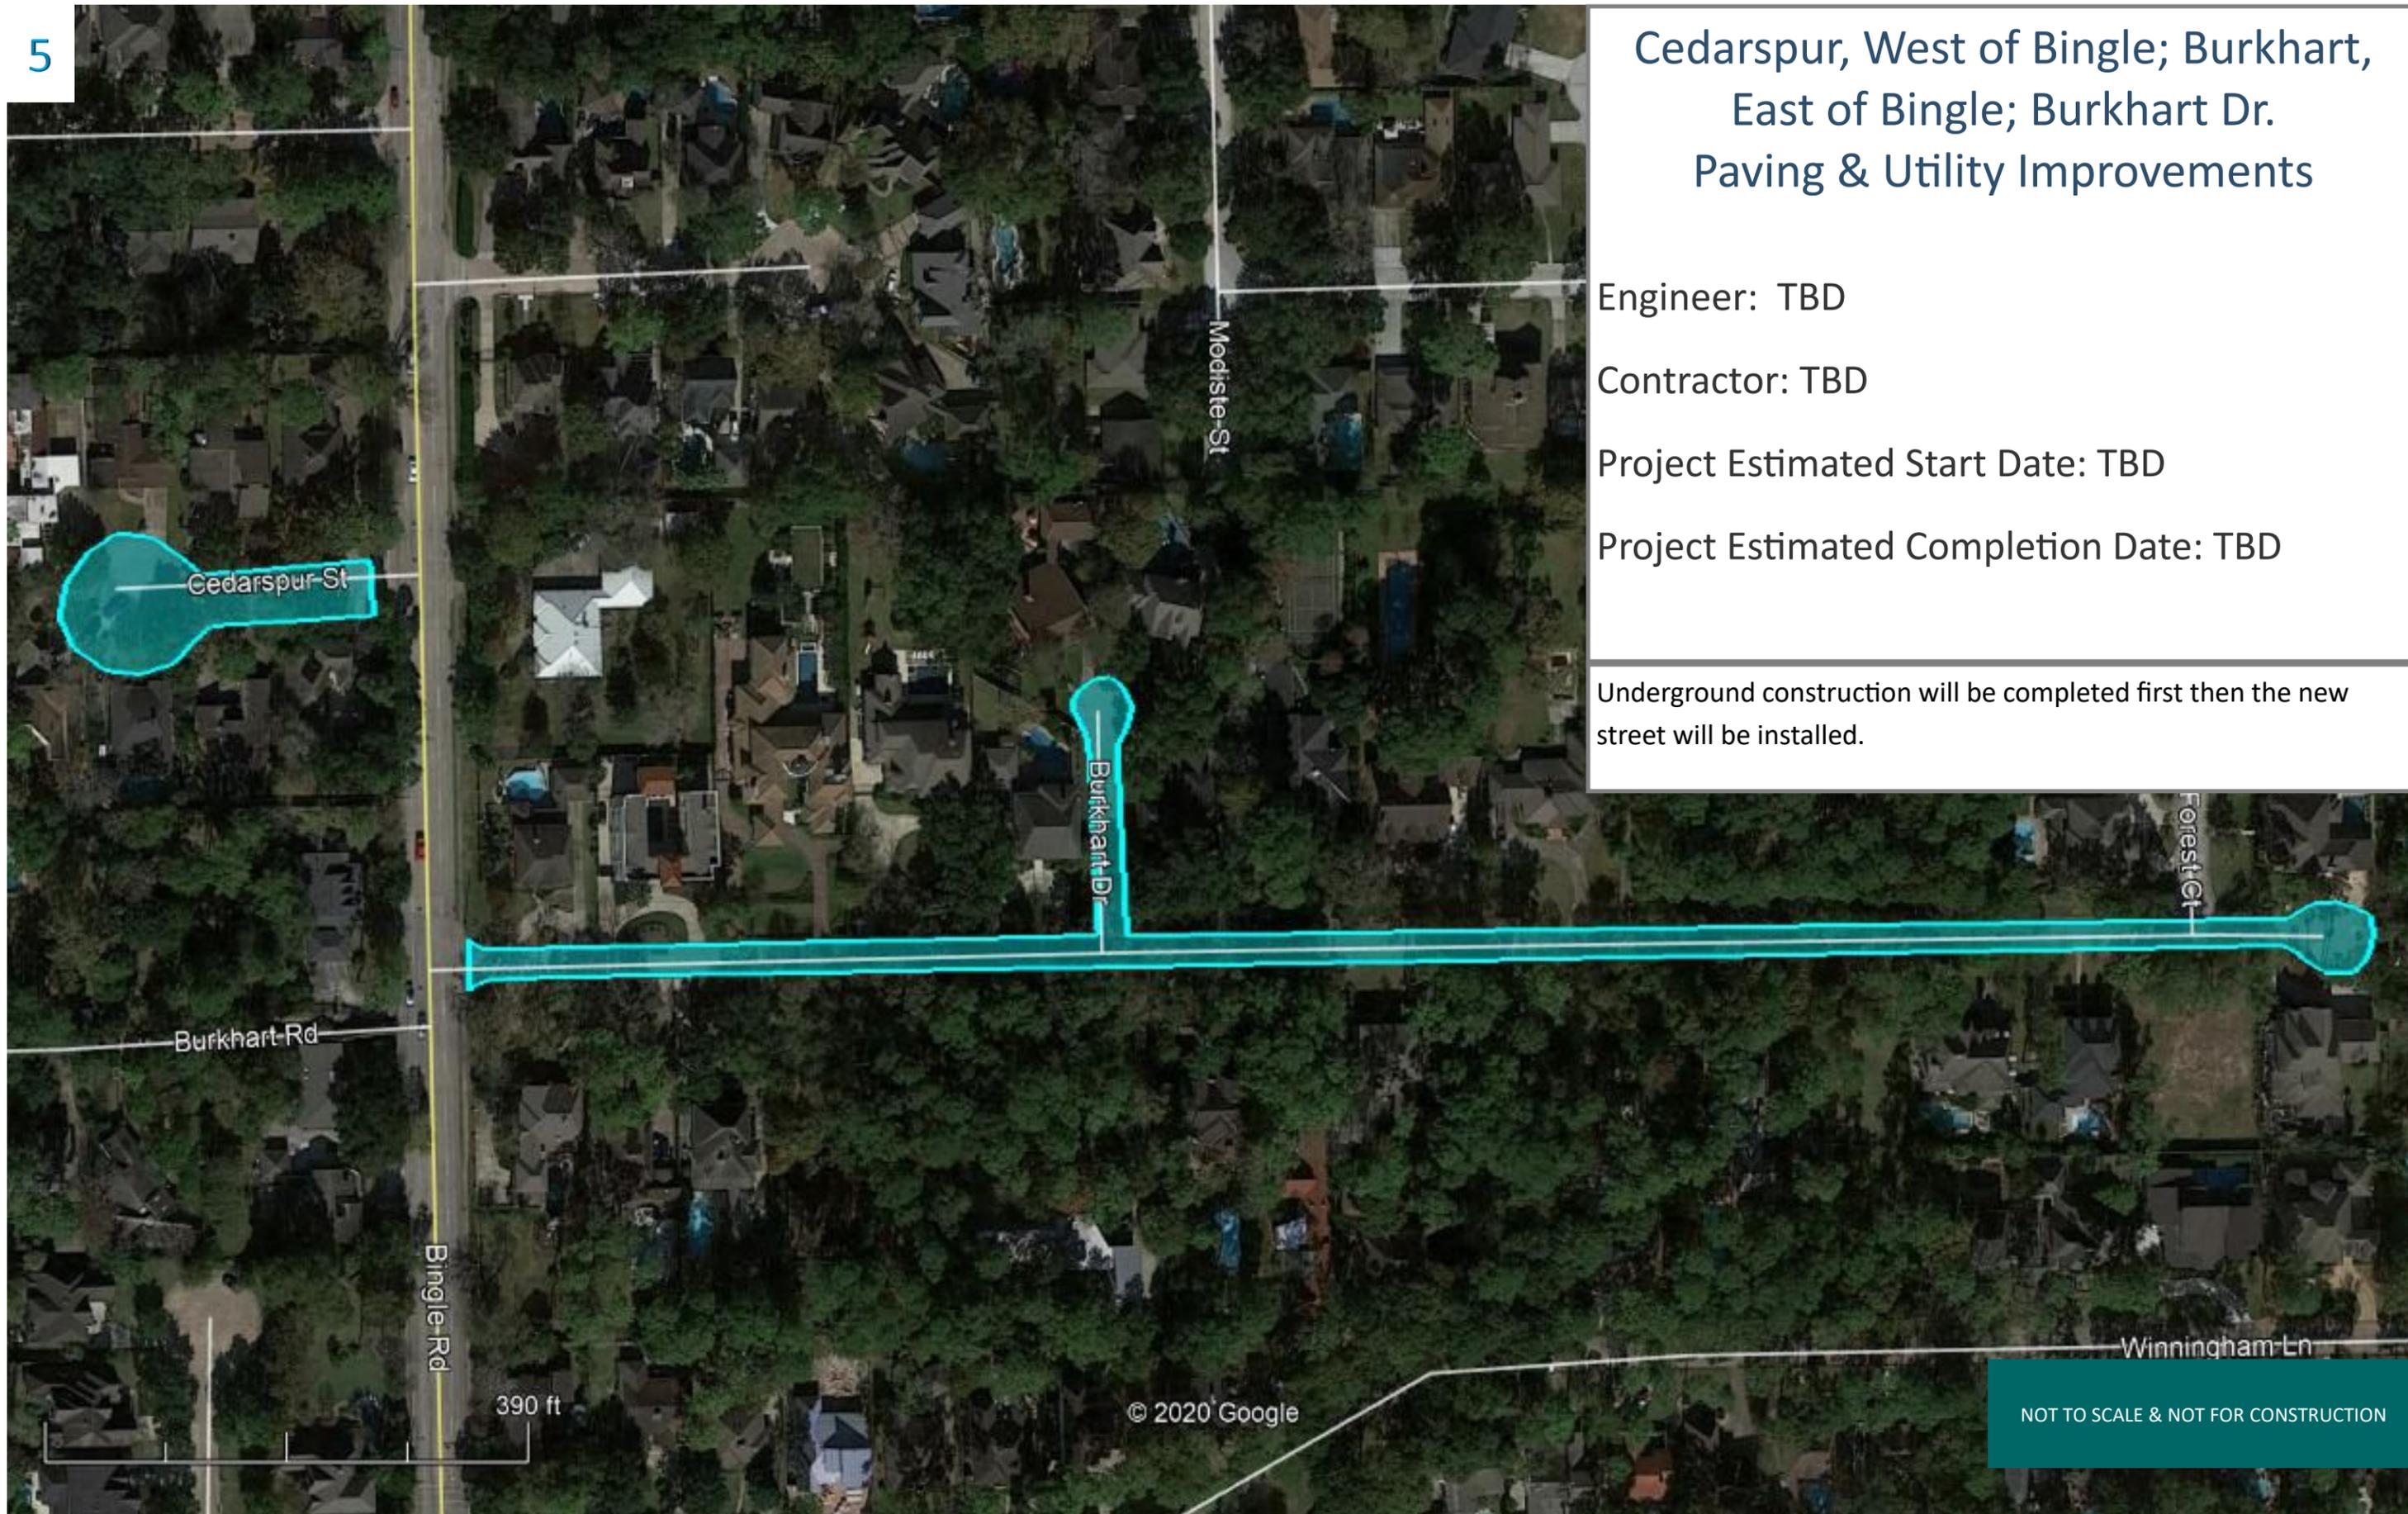

## Cedarspur, West of Bingle; Burkhardt, East of Bingle; Burkhardt Dr. Paving & Utility Improvements

Engineer: TBD

Contractor: TBD

Project Estimated Start Date: TBD

Project Estimated Completion Date: TBD

Underground construction will be completed first then the new street will be installed.

NOT TO SCALE & NOT FOR CONSTRUCTION

Cedar Spur Dr.; Peck Rd between Cedarspur St. & Winningham Ln; Burkhardt Cir. & Burkhardt Ct.; Winningham Ln east of Bingle Rd; Krist Dr.  
Pavement & Utility Improvements


Engineer: TBD

Contractor: TBD

Project Estimated Start Date: TBD

Project Estimated Completion Date: TBD

Underground construction will be completed first then the new street will be installed.

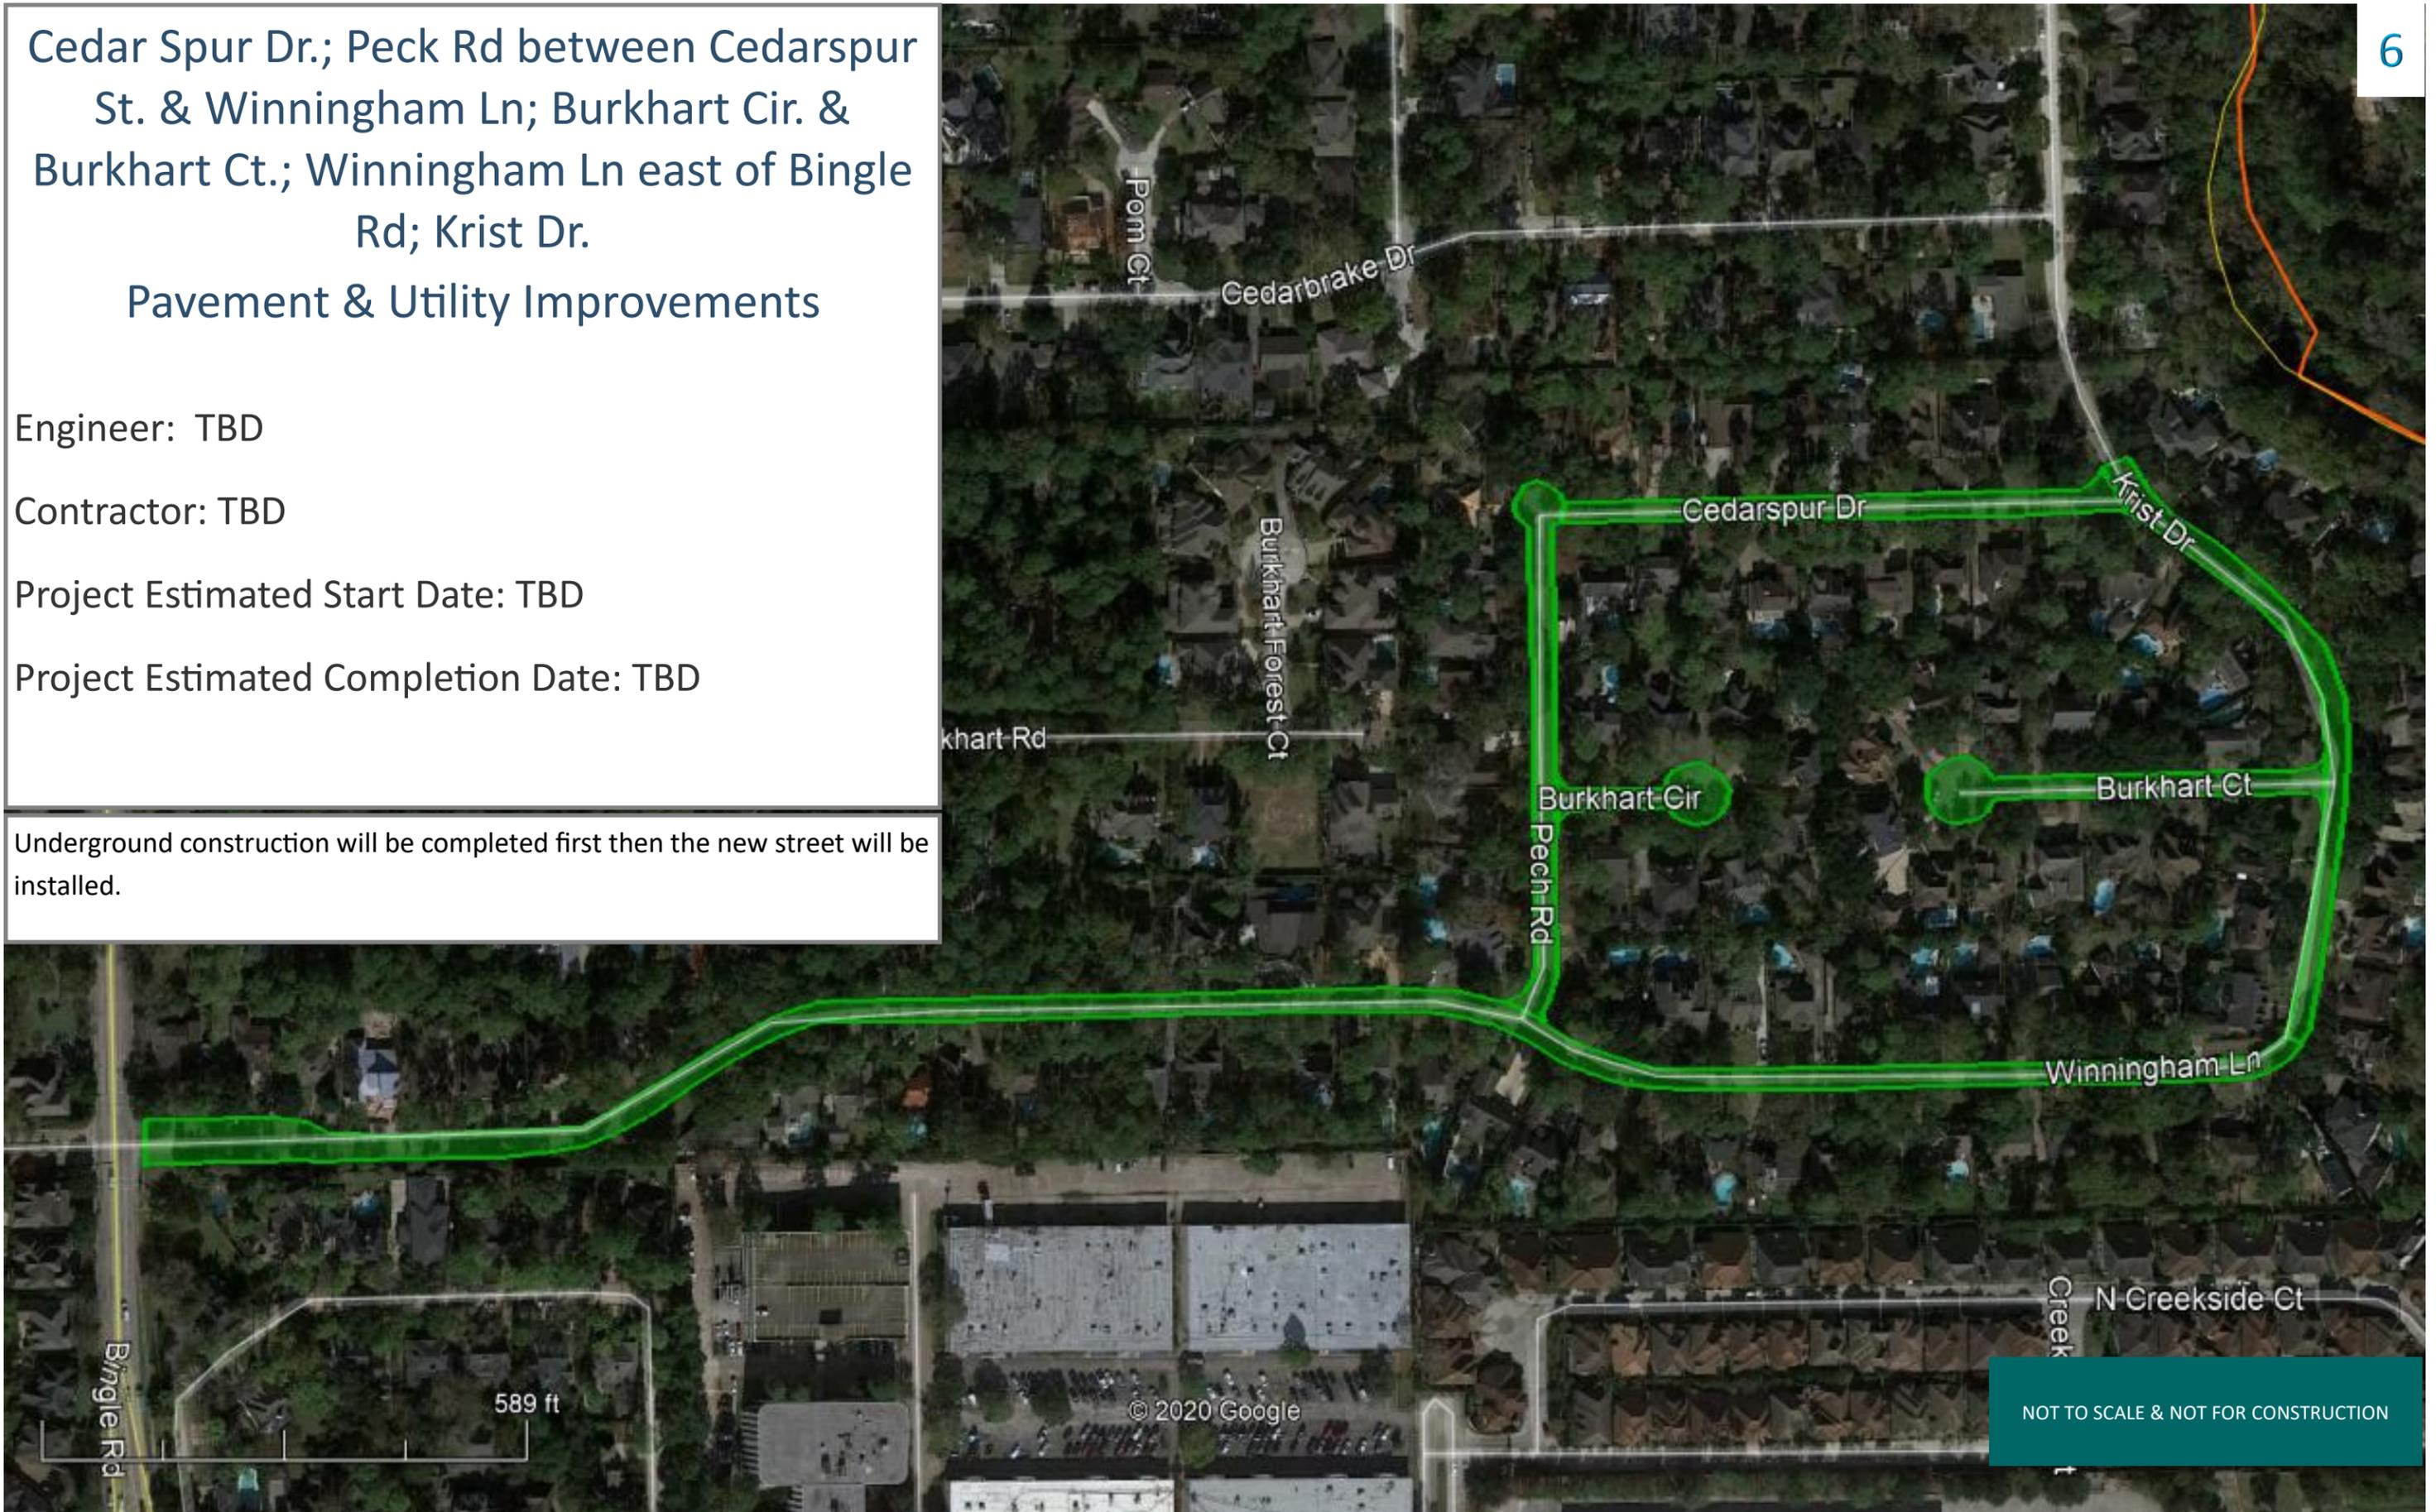

NOT TO SCALE & NOT FOR CONSTRUCTION
